



# Latest results from the efficiency scan 17/01/2011

Nicolas Zaganidis, Ian Crotty, Luigi Boccia

# Strips Numbering

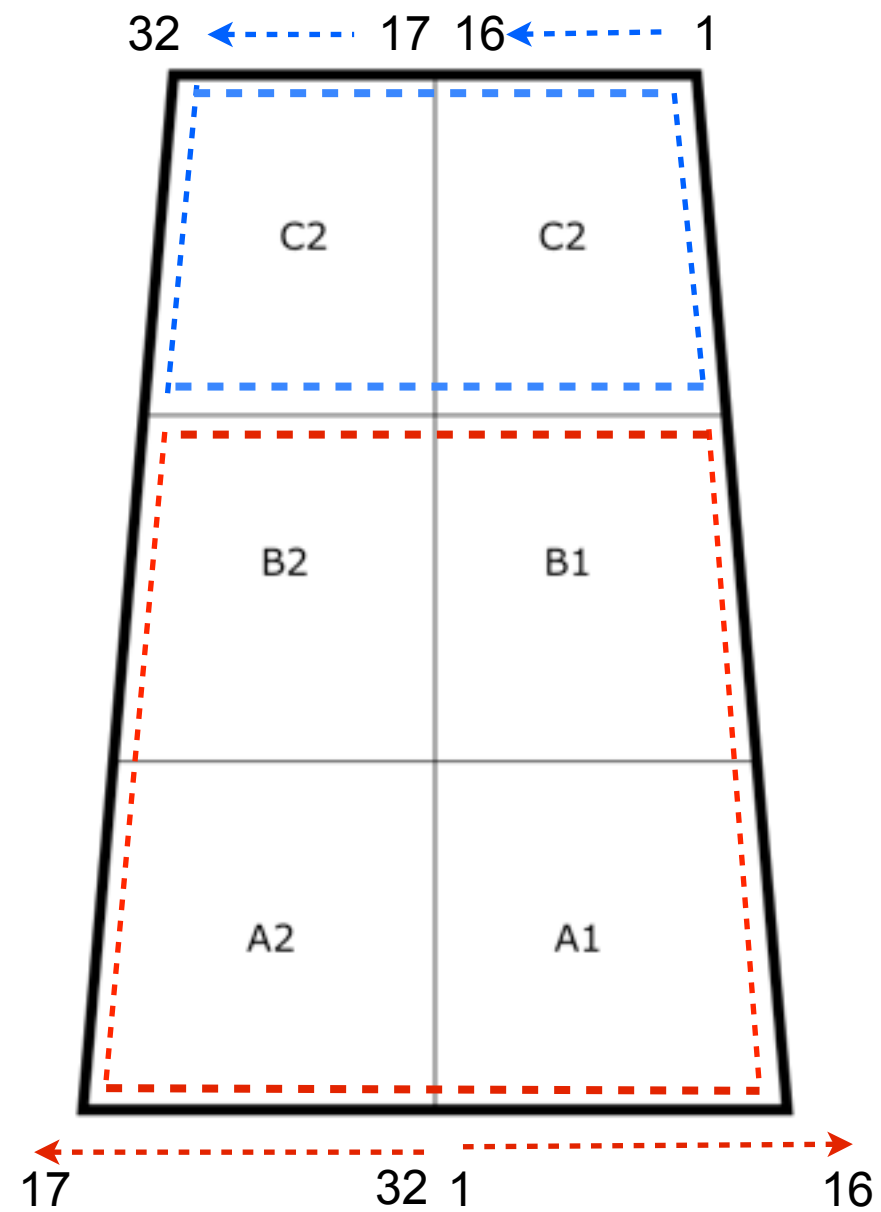

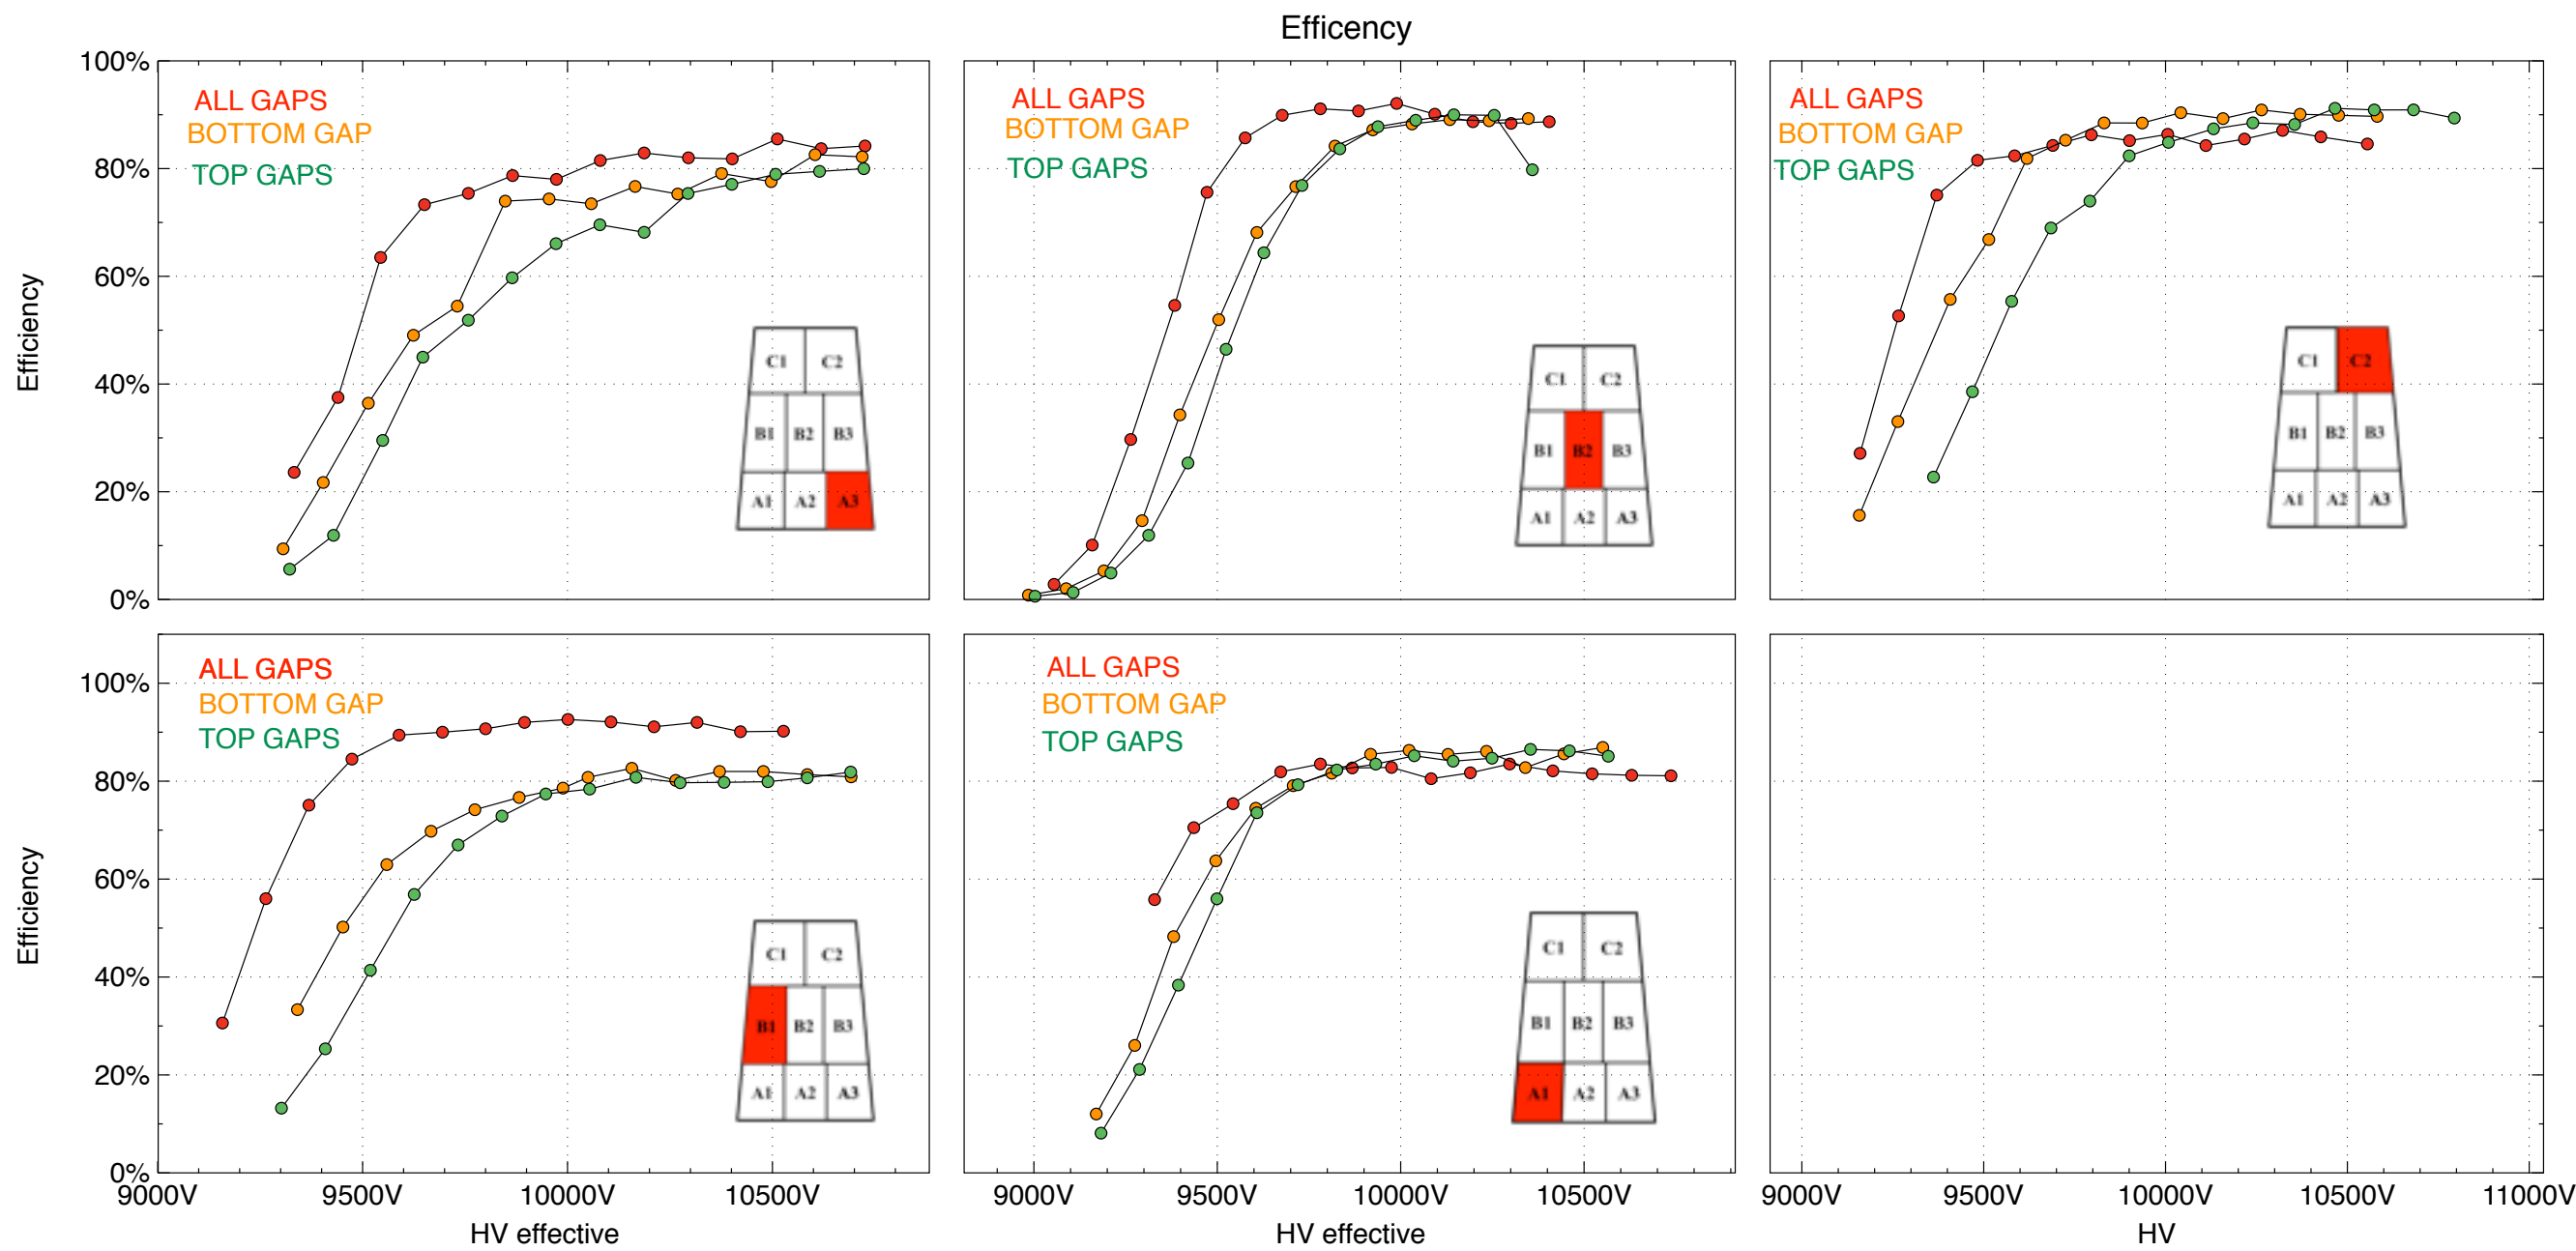

| Position of PM                                                                            | A1    | A2 | A3    | B1    | B2    | B3 | C1 | C2    |
|-------------------------------------------------------------------------------------------|-------|----|-------|-------|-------|----|----|-------|
| Strips Covered                                                                            | 21-28 |    | 11-16 | 21-29 | 2-10  |    |    | 9-15  |
| Efficinecy at operative HV effective 10 kV<br>(corresponding HV=9.5 kV)<br>for ALL GAPS   | 80,5% |    | 81,5% | 92,6% | 90,1% |    |    | 86,4% |
| Efficinecy at operative HV effective 10 kV<br>(corresponding HV=9.5 kV)<br>for BOTTOM GAP | 82,6% |    | 76,7% | 90,4  | 84,2% |    |    | 86,3% |
| Efficinecy at operative HV effective 10 kV<br>(corresponding HV=9.5 kV)<br>for TOP GAPS   | 80,8% |    | 68,2% | 88,5% | 83,7% |    |    | 85,2% |
